A PRACTICAL PLAN FOR THE GARDEN TEAM

Production plan - Ubhejane Crèche garden

November 2026 to October 2027

LOCATION	CLIMATE	PLAN PERIOD	GENERATED
This site (satellite climate records)	**Hot area, no frost - summer rain**	**November 2026 to October 2027**	**11 November 2026**

A crop plan should reduce uncertainty. It should show the garden team what to prepare, plant, harvest and buy - without making them decode the system behind it.

128.0 m²
growing space
7 beds + 4 staple plots

69.1 kg
known benchmark total
every planned crop cycle counted once; not the harvest of the plan year

0.54 kg/m²
benchmark density
known total ÷ whole growing area, to compare plans

Not calculated
loss-adjusted total
confirm a loss allowance from actual records

1/12
fresh-picking months
timing windows only; no monthly kg inferred

PLAN SIGNALS

- Tomatoes has the largest known benchmark volume at 12.0 kg.
- Peppers follows in the benchmark comparison at 8.0 kg.
- Jan, Aug, Sep carry the most planned jobs - counted as jobs, not hours.
- 100 bed-months of the year have no crop in the ground.

DECISIONS TO MAKE

- Compare the tomatoes benchmark with actual harvest records before planning storage or sales.
- Check actual household demand and recorded harvests; the benchmark comparison is not a meal or surplus guarantee.
- Check who is available before the Jan-Sep job peak, and time the work against real hours.
- Confirm a loss allowance from actual records before calculating a usable total.

How the totals are calculated

Only crops with a verified kg/m² entry are added to the conservative commercial benchmark comparison. Known total 69.1 kg; no loss-adjusted total is calculated until an allowance is confirmed.

This total counts every planned crop cycle once, whenever its first picking falls, including cycles first picked after the plan year shown on the cover. It is not the harvest of that year. The year-by-year table groups the same crop cycles by the year of first picking.

This is a benchmark comparison, not a household or farm-yield guarantee. Record actual harvests and losses on the monthly record sheet.

HOW MUCH TO TRUST THIS PLAN

No agronomist has checked this plan. It is built from your own map, from climate and soil data measured by satellites and global models, and from published South African growing guidelines. It is put together carefully and in good faith - but it is a starting point, not an instruction.

Use your own judgement alongside it. A computer cannot see your land. It does not know where the water stands after heavy rain, which corner the frost settles in, what failed here last year, or what your family will actually eat. You do.

Soil is the figure most likely to be wrong. Ours comes from a global model that reads a wide area, and real soil can change from one end of a single field to the other. If any number here matters to a decision you are spending money on, a soil test is the only way to know. You can upload one and the plan will be rebuilt around your real numbers.

Show this to your local agricultural extension officer. They know your district, your rainfall and your pests in a way no model does, and they can correct in ten minutes what would otherwise cost you a season. It costs nothing, and it is the single most useful thing you can do with this document.

Expect some of it to be wrong. Write down what you actually planted and what you actually harvested. Every season you record makes the next plan fit your land more closely than this one does - that is the point of it.

Published optimum-condition maturity endpoints are planning slots, not promises. Before any successor is sown or transplanted, confirm the previous crop is finished and the bed is actually clear; crops may mature later.

MANAGER VIEW

The year in numbers


Use this page to compare benchmark timing with labour, kitchen demand, storage and mentoring visits before the work reaches the field.

CROP-CYCLE BENCHMARK ONLY

The 69.1 kg figure is a sum of crop-cycle benchmarks. It is not divided into months because the source does not provide a within-window picking curve.

1 of 12 months have at least one verified fresh-picking window; that is timing, not monthly kilograms.

Workload by month (jobs planned)

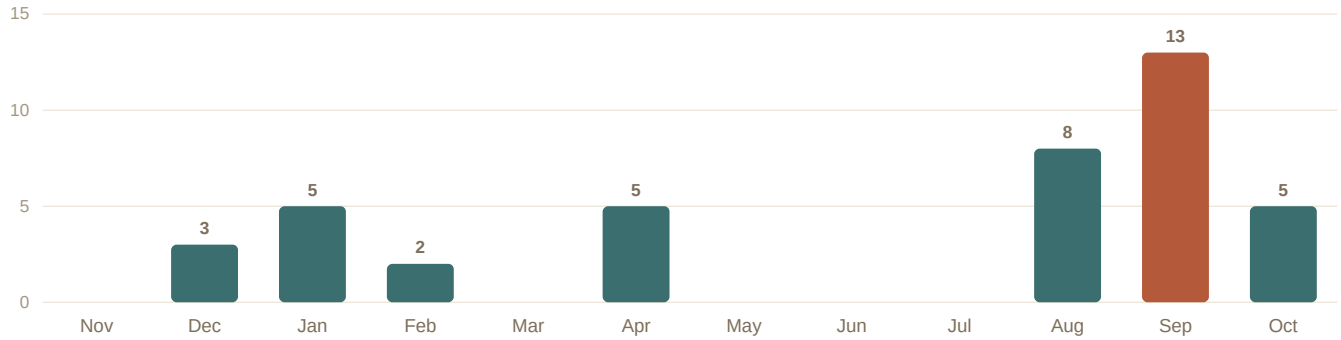

Largest crops by known benchmark volume

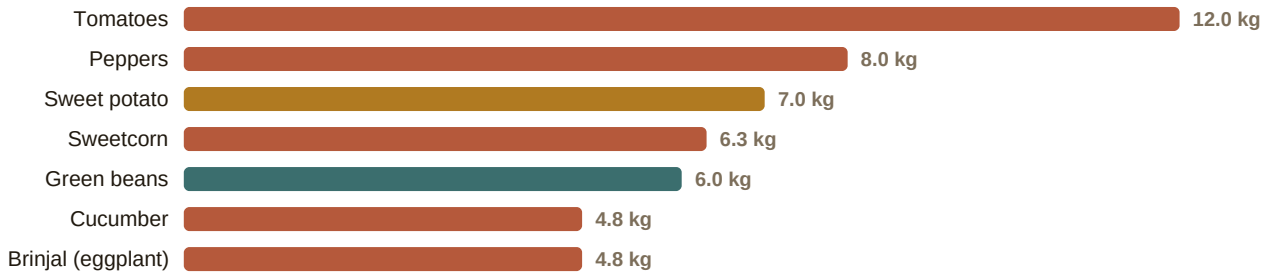


Chart note: the workload chart counts planned jobs, not hours - a plot of maize and a bed of lettuce each count as one. Crop-cycle benchmark weights are shown by crop only; no monthly kg or Rand is inferred.

BED CALENDAR

Growing plan: Nov 2026 - Oct 2027

Read across to see what occupies each bed. Each line is one planting, not a measured strip of land.

Bed reserved / growing Pick fresh food Finish a cover crop

Tray crops reserve the bed from their first readiness month. Follow the monthly jobs. An arrow means the crop continues after Oct 2027.

CROP / SHARE OF BED	Nov 2026	Dec 2026	Jan 2027	Feb 2027	Mar 2027	Apr 2027	May 2027	Jun 2027	Jul 2027	Aug 2027	Sep 2027	Oct 2027
Bed 1												6 m²
GB **Green beans** 1/3 area - sow Feb 2027						Pick						
Pe **Peppers** 1/3 area - sow Sep 2027												→
Tu **Turnips** 1/3 area - sow Sep 2027												→
Sp **Spanspek (sweet melon)** 1/3 area - sow Sep 2027												→
Sw **Sweetcorn** 1/3 area - sow Jan 2027						Pick						
Bed 2												6 m²
Ca **Carrots** 1/3 area - sow Sep 2027												→
Be **Beetroot** 1/3 area - sow Sep 2027												→
Br **Brinjal (eggplant)** 1/3 area - sow Aug 2027												→

BED CALENDAR - CONTINUED

Growing plan: Nov 2026 - Oct 2027

Read across to see what occupies each bed. Each line is one planting, not a measured strip of land.

Bed reserved / growing Pick fresh food Finish a cover crop

Tray crops reserve the bed from their first readiness month. Follow the monthly jobs. An arrow means the crop continues after Oct 2027.

CROP / SHARE OF BED	Nov 2026	Dec 2026	Jan 2027	Feb 2027	Mar 2027	Apr 2027	May 2027	Jun 2027	Jul 2027	Aug 2027	Sep 2027	Oct 2027
Bed 2 - continued												6 m²
GB **Green beans** — Whole area - sow Feb 2027						Pick						
Bed 3												6 m²
To **Tomatoes** — 1/3 area - sow Aug 2027												
Pa **Parsley** — 1/3 area - sow Sep 2027												
GS **Gem squash** — 1/3 area - sow Sep 2027												
Sw **Sweetcorn** — 67% area - sow Jan 2027						Pick						
Bed 4												6 m²
To **Tomatoes** — 1/3 area - sow Sep 2027												
Cu **Cucumber** — 1/3 area - sow Sep 2027												

BED CALENDAR - CONTINUED

Growing plan: Nov 2026 - Oct 2027

Read across to see what occupies each bed. Each line is one planting, not a measured strip of land.

Bed reserved / growing Pick fresh food Finish a cover crop

Tray crops reserve the bed from their first readiness month. Follow the monthly jobs. An arrow means the crop continues after Oct 2027.

CROP / SHARE OF BED	Nov 2026	Dec 2026	Jan 2027	Feb 2027	Mar 2027	Apr 2027	May 2027	Jun 2027	Jul 2027	Aug 2027	Sep 2027	Oct 2027
Bed 4 - continued												6 m²
Sw **Sweetcorn** 1/2 area - sow Jan 2027						Pick						
GB **Green beans** 1/3 area - sow Sep 2027												
Bed 5												6 m²
SP **Sweet potato** 1/3 area - sow Sep 2027												
Cu **Cucumber** 1/3 area - sow Oct 2027												
Br **Brinjal (eggplant)** 1/3 area - sow Sep 2027												
GB **Green beans** 1/3 area - sow Feb 2027						Pick						
Bed 6												8 m²
SP **Sweet potato** 1/3 area - sow Oct 2027												

BED CALENDAR - CONTINUED

Growing plan: Nov 2026 - Oct 2027

Read across to see what occupies each bed. Each line is one planting, not a measured strip of land.

Bed reserved / growing Pick fresh food Finish a cover crop

Tray crops reserve the bed from their first readiness month. Follow the monthly jobs. An arrow means the crop continues after Oct 2027.

CROP / SHARE OF BED	Nov 2026	Dec 2026	Jan 2027	Feb 2027	Mar 2027	Apr 2027	May 2027	Jun 2027	Jul 2027	Aug 2027	Sep 2027	Oct 2027
Bed 6 - continued												8 m²
Le **Lettuce** 1/3 area - sow Aug 2027											▶	▶
Gr **Groundnuts (peanuts)** 1/3 area - sow Sep 2027											▶	▶
Bed 7												6 m²
Pe **Peppers** 1/3 area - sow Aug 2027											▶	▶
Gr **Groundnuts (peanuts)** 1/3 area - sow Oct 2027												▶
GS **Gem squash** 1/3 area - sow Oct 2027												▶
Plot 1												21 m²
No dated crop reserved here												

BED CALENDAR - CONTINUED

Growing plan: Nov 2026 - Oct 2027

Read across to see what occupies each bed. Each line is one planting, not a measured strip of land.

Bed reserved / growing Pick fresh food Finish a cover crop

Tray crops reserve the bed from their first readiness month. Follow the monthly jobs. An arrow means the crop continues after Oct 2027.

CROP / SHARE OF BED	Nov 2026	Dec 2026	Jan 2027	Feb 2027	Mar 2027	Apr 2027	May 2027	Jun 2027	Jul 2027	Aug 2027	Sep 2027	Oct 2027
Plot 2												21 m²
No dated crop reserved here												
Plot 3												21 m²
No dated crop reserved here												
Plot 4												21 m²
No dated crop reserved here												

UBHEJANE CRÈCHE GARDEN

Nov 2026 - Oct 2027

Fruit, nuts and berries: solid marks are local dates. Outlined marks: references when established, not food promised this year.

This site (satellite climate records) - Hot area, no frost - summer rain

CROP / FOOD SOURCE	Nov NOW	Dec 2026	Jan 2027	Feb 2027	Mar 2027	Apr 2027	May 2027	Jun 2027	Jul 2027	Aug 2027	Sep 2027	Oct 2027
Fresh veg												
GB Green beans						GB						
Sw Sweetcorn						Sw						
Staple crops												
No staple picking months marked yet.												
Food forest - fruit, nuts & berries and other foods	When established											
No confirmed picking months shown. Check fruit, nuts and berries on your map in the app.												
Animal products												
No confirmed production months shown. Check animal products and housing on your map in the app.												
Growing space used	0%	0%	7%	15%	15%	15%	0%	0%	0%	0%	23%	34%

Outlined bands are planning references when established; they do not enter food totals or picking jobs. Blank months have no picking window marked. Recorded planting ages keep young plants out of early reference months. Check plant ages and Food sources to check in the app. Gold rows require each crop's storage conditions; check the full plan or app. Red space figures mean the plan needs more growing space than is mapped.

UBHEJANE CRÈCHE GARDEN

Before using stored food

The storage row applies only when these sourced conditions are met. Check the food before using it.

Sweet potato - sourced storage window: 3 months

Only mature, undamaged roots; cured 30-32°C/85-90% RH for 4-7 days, then stored with minimal handling as cool as achievable (source optimum 13°C) at ~85-90% RH. The sweet potato weevil (Cylas spp.) is the main storage threat.

Source guide

Groundnuts (peanuts) - sourced storage window: 6 months

Unshelled (in-shell) pods dried to in-shell moisture ~10% or less, stored in gunny bags, mud bins, baskets or a ventilated dry room, protected from pests and damp.

Source guide

Not checked by an agronomist - a planning guide, not an instruction. Show it to your extension officer, and get a soil test before spending on soil.


Published optimum-condition maturity endpoints are planning slots, not promises. Before any successor is sown or transplanted, confirm the previous crop is finished and the bed is actually clear; crops may mature later.

UBHEJANE CRÈCHE GARDEN


Fresh food, kept food and space

Known food options by month. Counted once per crop or product, not kilograms, portions or meals.


1. Fresh food (food kinds)



2. Fresh food + kept food (food kinds)



3. Used and free crop-growing space (m2)

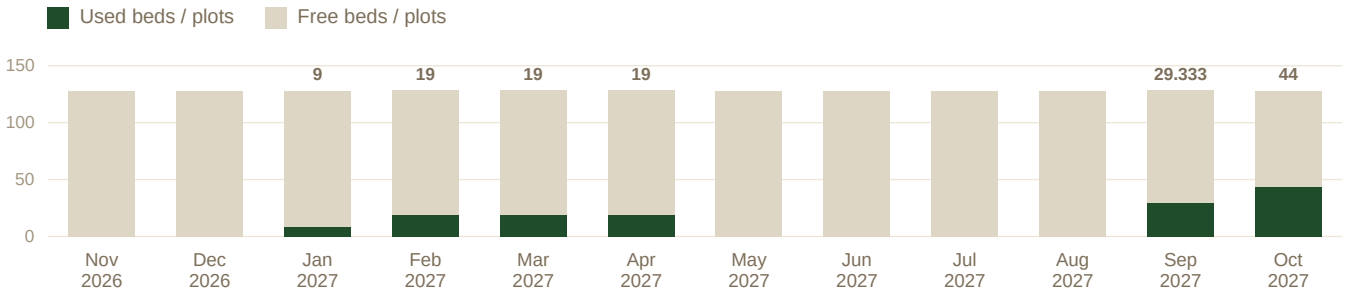

The two food charts share a scale. A crop present fresh and kept still counts once; kept colours add other food kinds. Dated output records update fresh counts. Research season references and sources without local dates are outside food counts.

Pantry storage requires each crop's source conditions. Preserved stock is shown only for recorded months; no amount, recipe or safe shelf life is inferred.

No preservation records supplied. Frozen, dried, fermented and processed food are not inferred from fresh harvest.

Space is for 128 m2 of mapped beds and plots only; trees, animal housing and ponds are outside this area. Numbers above space bars show used m2.


UBHEJANE CRÈCHE GARDEN

Production weights and missing records

Monthly records, crop-cycle benchmarks and food kept in stock are separate measures. Missing quantities are not zero.

Monthly production kg are not recorded. The crop-cycle graph below is a planning benchmark; it does not fill in missing monthly harvest weights.

Crop-cycle kg by first picking month (full-cycle kg)

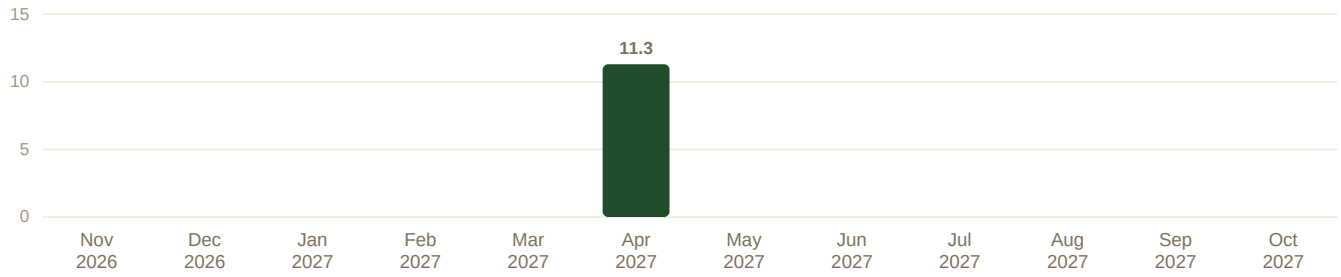

Each bar groups the entire crop-cycle benchmark by the month picking starts. It is not the weight harvested in that month. The source does not supply a monthly picking curve; quantities are not divided across a picking window.

No monthly quantities are recorded for this dated year in kg, eggs, litres, items or kept-stock kg. Enter expected or actual amounts in the app; the printed monthly table appears once a quantity is recorded, including zero.

? means quantity not recorded, not zero. * marks a known stock subtotal with missing batch weights. Egg counts and litres use actual records where entered, otherwise expected records. They are never converted to kg. Stock kg are food already held; they are never added to new production.

Monthly quantities still needed: Green beans, Sweetcorn. Research season references do not establish a harvest weight.

UBHEJANE CRÈCHE GARDEN

Before you buy or start

Use your farm observations and the research shortlists. Confirm choices locally before buying.

Research climate group: Growing area not resolved. This grouping is not a validated recommendation for this farm.

What you reported about this farm

Water through the dry season

Not recorded. Complete the site survey and confirm water before choosing an intensive plan.

Frost on this farm

Frost has been observed here in Apr, Jul, Dec. Check frost-tender crops against these observations.

Sun and drainage

Sun: not recorded.

Drainage: not recorded. Soil-test results and crop-specific needs still need checking.

Planned crops to check for frost

Green beans: Apr.

Sweetcorn: Apr.

These planned crops will hold ground in months when frost has been observed here. Confirm local protection or change the planting before relying on these dates.

Crop varieties to check locally

Keep the named variety you actually choose. Research shortlists need confirmation for your local season, water and ground.

Green beans

Recorded variety: not chosen yet.

This site's climate has not resolved, so no local shortlist is claimed. Open the crop card to see sources and record your choice.

Carrots

Recorded variety: not chosen yet.

This site's climate has not resolved, so no local shortlist is claimed. Open the crop card to see sources and record your choice.

Tomatoes

Recorded variety: not chosen yet.

This site's climate has not resolved, so no local shortlist is claimed. Open the crop card to see sources and record your choice.

Sweet potato

Recorded variety: not chosen yet.

This site's climate has not resolved, so no local shortlist is claimed. Open the crop card to see sources and record your choice.

Peppers

Recorded variety: not chosen yet.

This site's climate has not resolved, so no local shortlist is claimed. Open the crop card to see sources and record your choice.

UBHEJANE CRÈCHE GARDEN

Farm choices - continued

Use your farm observations and the research shortlists. Confirm choices locally before buying.

Crop varieties to check locally (continued)

Beetroot

Recorded variety: not chosen yet.

This site's climate has not resolved, so no local shortlist is claimed. Open the crop card to see sources and record your choice.

Parsley

Recorded variety: not chosen yet.

This site's climate has not resolved, so no local shortlist is claimed. Open the crop card to see sources and record your choice.

Cucumber

Recorded variety: not chosen yet.

This site's climate has not resolved, so no local shortlist is claimed. Open the crop card to see sources and record your choice.

Lettuce

Recorded variety: not chosen yet.

This site's climate has not resolved, so no local shortlist is claimed. Open the crop card to see sources and record your choice.

Brinjal (eggplant)

Recorded variety: not chosen yet.

This site's climate has not resolved, so no local shortlist is claimed. Open the crop card to see sources and record your choice.

Groundnuts (peanuts)

Recorded variety: not chosen yet.

This site's climate has not resolved, so no local shortlist is claimed. Open the crop card to see sources and record your choice.

Turnips

Recorded variety: not chosen yet.

This site's climate has not resolved, so no local shortlist is claimed. Open the crop card to see sources and record your choice.

Gem squash

Recorded variety: not chosen yet.

This site's climate has not resolved, so no local shortlist is claimed. Open the crop card to see sources and record your choice.

Spanspek (sweet melon)

Recorded variety: not chosen yet.

This site's climate has not resolved, so no local shortlist is claimed. Open the crop card to see sources and record your choice.

UBHEJANE CRÈCHE GARDEN

Farm choices - continued

Use your farm observations and the research shortlists. Confirm choices locally before buying.

Crop varieties to check locally (continued)

Sweetcorn

Recorded variety: not chosen yet.

This site's climate has not resolved, so no local shortlist is claimed. Open the crop card to see sources and record your choice.

FULL PLAN

Bed-by-bed plan

Each line is one planting. Yield is a conservative benchmark comparison where a verified kg/m² entry exists; "Not verified" is never treated as 0kg.

Area	Crop	Space	Establish	Into field	Harvest	Benchmark
Bed 1	Sweetcorn	1/3	Direct sow Jan	Direct	Apr - Frost-tender: still in the ground in Apr, when you recorded frost.	1.4 kg
	Green beans	1/3	Direct sow Feb	Direct	Apr - Frost-tender: still in the ground in Apr, when you recorded frost.	1.0 kg
	Peppers	1/3	Nursery Sep	Check Oct-Dec; transplant when ready	Feb-Apr	4.0 kg
	Spanspek (sweet melon)	1/3	Direct sow Sep	Direct	Jan	2.4 kg
	Turnips	1/3	Direct sow Sep	Direct	Dec	2.0 kg
Bed 2	Green beans	Full	Direct sow Feb	Direct	Apr - Frost-tender: still in the ground in Apr, when you recorded frost.	3.0 kg
	Brinjal (eggplant)	1/3	Nursery Aug	Check Sep-Nov; transplant when ready	Jan	2.4 kg
	Beetroot	1/3	Direct sow Sep	Direct	Dec-Jan	2.8 kg
	Carrots	1/3	Direct sow Sep	Direct	Jan	4.0 kg
Bed 3	Sweetcorn	67%	Direct sow Jan	Direct	Apr - Frost-tender: still in the ground in Apr, when you recorded frost.	2.8 kg
	Tomatoes	1/3	Nursery Aug	Check Sep-Nov; transplant when ready	Jan-Mar	6.0 kg

Bed-by-bed plan (continued)

Area	Crop	Space	Establish	Into field	Harvest	Benchmark
Bed 3	Gem squash	1/3	Direct sow Sep	Direct	Dec	2.4 kg
	Parsley	1/3	Direct sow Sep	Direct	Dec	0.4 kg
Bed 4	Sweetcorn	1/2	Direct sow Jan	Direct	Apr - Frost-tender: still in the ground in Apr, when you recorded frost.	2.1 kg
	Cucumber	1/3	Direct sow Sep	Direct	Dec	2.4 kg
	Green beans	1/3	Direct sow Sep	Direct	Nov	1.0 kg
	Tomatoes	1/3	Nursery Sep	Check Oct-Dec; transplant when ready	Feb-Apr	6.0 kg
Bed 5	Green beans	1/3	Direct sow Feb	Direct	Apr - Frost-tender: still in the ground in Apr, when you recorded frost.	1.0 kg
	Brinjal (eggplant)	1/3	Nursery Sep	Check Oct-Dec; transplant when ready	Feb	2.4 kg
	Sweet potato	1/3	Plant slips Sep	Direct	Feb-Mar	3.0 kg
	Cucumber	1/3	Direct sow Oct	Direct	Jan	2.4 kg
Bed 6	Lettuce	1/3	Nursery Aug	Check Sep-Nov; transplant when ready	Jan	3.2 kg
	Groundnuts (peanuts)	1/3	Direct sow Sep	Direct	Mar	0.3 kg
	Sweet potato	1/3	Plant slips Oct	Direct	Mar-Apr	4.0 kg
Bed 7	Peppers	1/3	Nursery Aug	Check Sep-Nov; transplant when ready	Jan-Mar	4.0 kg

Bed-by-bed plan (continued)

Area	Crop	Space	Establish	Into field	Harvest	Benchmark
Bed 7	Gem squash	1/3	Direct sow Oct	Direct	Jan	2.4 kg
	Groundnuts (peanuts)	1/3	Direct sow Oct	Direct	Apr	0.2 kg

INPUTS

Seed and seedling buying schedule

Find the month, then the crop and bed. Check the seed quantity and sowing method before buying.

The buying rule

Source direct-sown or tray seed before the named sowing month; the source does not provide a universal procurement lead time. Ready-grown seedlings are listed at the start of the field-readiness window; buy them only when the bed and seedlings are ready. Living corms, slips, cloves and seed potatoes are listed close to planting. For a tray crop, choose either packet seed for the nursery or ready-grown seedlings - not both.

A published field seed rate gives a weight range for the mapped area. Confirm the sowing method with the supplier; no germination or loss allowance is added. For crops without a published seed rate, field spacing supports only an approximate FINAL stand. It does not prove a seed-buying quantity: use the packet's crop-specific sowing rate and germination guidance. Living-material ranges are approximate field positions from mapped area and published spacing, not guaranteed order quantities or loss allowances; supplier and crop-specific guidance may change what to purchase.

Source/check	Crop	Quantity	Method	For	Planting timeline
January 2027	Sweetcorn	10.8-13.5 g seed	Published field seed rate; confirm sowing method	Beds 1, 3, 4	Sow Jan
February 2027	Green beans	Packet rate needed	Direct sow; ~238-556 final positions	Beds 1, 2, 5	Sow Feb
September 2027	Carrots	Packet rate needed	Direct sow; ~99-500 final positions	Bed 2	Sow Sep
	Beetroot	Packet rate needed	Direct sow; ~95-200 final positions	Bed 2	Sow Sep
	Groundnuts (peanuts)	Packet rate needed	Direct sow; ~79-178 final positions	Bed 6	Sow Sep
	Green beans	Packet rate needed	Direct sow; ~47-112 final positions	Bed 4	Sow Sep

Seed and seedling buying schedule (continued)

Source/check	Crop	Quantity	Method	For	Planting timeline
September 2027	Turnips	Packet rate needed	Direct sow; ~41-63 final positions	Bed 1	Sow Sep
	Lettuce	~15-27 seedlings positions	Ready seedlings; own seed before Aug nursery	Bed 6	Source own seed before Aug; nursery Aug; check/transplant Sep-Nov
	Peppers	~5-9 seedlings positions	Ready seedlings; own seed before Aug nursery	Bed 7	Source own seed before Aug; nursery Aug; check/transplant Sep-Nov
	Sweet potato	~5-9 slips positions	Living pieces; confirm loss allowance	Bed 5	Sow Sep
	Brinjal (eggplant)	~5-6 seedlings positions	Ready seedlings; own seed before Aug nursery	Bed 2	Source own seed before Aug; nursery Aug; check/transplant Sep-Nov
	Cucumber	Packet rate needed	Direct sow; ~2-5 final positions	Bed 4	Sow Sep
	Tomatoes	~2-8 seedlings positions	Ready seedlings; own seed before Aug nursery	Bed 3	Source own seed before Aug; nursery Aug; check/transplant Sep-Nov
	Gem squash	0.4-0.6 g seed	Published field seed rate; confirm sowing method	Bed 3	Sow Sep
	Parsley	0.6 g seed	Published field seed rate; confirm sowing method	Bed 3	Sow Sep

Seed and seedling buying schedule (continued)

Source/check	Crop	Quantity	Method	For	Planting timeline
September 2027	Spanspek (sweet melon)	0.6 g seed	Published field seed rate; confirm sowing method	Bed 1	Sow Sep
October 2027	Groundnuts (peanuts)	Packet rate needed	Direct sow; ~59-134 final positions	Bed 7	Sow Oct
	Sweet potato	~6-12 slips positions	Living pieces; confirm loss allowance	Bed 6	Sow Oct
	Peppers	~5-9 seedlings positions	Ready seedlings; own seed before Sep nursery	Bed 1	Source own seed before Sep; nursery Sep; check/transplant Oct-Dec
	Brinjal (eggplant)	~5-6 seedlings positions	Ready seedlings; own seed before Sep nursery	Bed 5	Source own seed before Sep; nursery Sep; check/transplant Oct-Dec
	Cucumber	Packet rate needed	Direct sow; ~2-5 final positions	Bed 5	Sow Oct
	Tomatoes	~2-8 seedlings positions	Ready seedlings; own seed before Sep nursery	Bed 4	Source own seed before Sep; nursery Sep; check/transplant Oct-Dec
	Gem squash	0.4-0.6 g seed	Published field seed rate; confirm sowing method	Bed 7	Sow Oct

Sweetcorn - check the sowing method

Published field rate: 12-15 kg/ha. The buying range uses the mapped area; no germination allowance is added.

Grown and eaten as a fresh vegetable, unlike field maize - the dossier's own food-group is fruiting vegetable, not staple grain, so it is kept there rather than lumped with maize despite the shared species. Tender to frost like maize.

Gem squash - check the sowing method

Published field rate: 2-3 kg/ha. The buying range uses the mapped area; no germination allowance is added.

Cucurbitaceae family, same as pumpkin, butternut, cucumber and watermelon - avoid repeating this family in the same bed. Frost-tender vine crop; no Western Cape sowing calendar was found even though it is a known WC crop, so treat that as a local-confirmation item.

Parsley - check the sowing method

Published field rate: 3 kg/ha. The buying range uses the mapped area; no germination allowance is added.

A biennial herb grown as an annual for its leaves. Apiaceae family, same as carrots - avoid repeating that family in the same bed too often.

Spanspek (sweet melon) - check the sowing method

Published field rate: 3 kg/ha. The buying range uses the mapped area; no germination allowance is added.

Cucurbitaceae melon vine. A January sowing is left off this catalog's planner because the resulting harvest would run into frost - still workable with local frost protection, just not auto-scheduled here.

ImbewuField

FIELD SHEET

December 2026 field sheet

Ubhejane Crèche garden - tick each job off as it is done.

3 jobs - 0 sowing / planting - 0 harvest / recording

DONE	PLACE	WORK TO COMPLETE	DATE / NOTE
Prepare for the next planting			
		Where a bed follows another crop, confirm it is finished and cleared before preparing it. Assess soil and drainage; use a soil test or local advice before adding amendments.	
☐	**Bed 1**	Prepare the ground for sweetcorn (a third of the bed; 2 m²).	
☐	**Bed 3**	Prepare the ground for sweetcorn (67% of the bed; 4 m²).	
☐	**Bed 4**	Prepare the ground for sweetcorn (half the bed; 3 m²).	

ImbewuField

FIELD SHEET

January 2027 field sheet

Ubhejane Crèche garden - tick each job off as it is done.

5 jobs - 3 sowing / planting - 0 harvest / recording

DONE	PLACE	WORK TO COMPLETE	DATE / NOTE
Prepare for the next planting			
		Where a bed follows another crop, confirm it is finished and cleared before preparing it. Assess soil and drainage; use a soil test or local advice before adding amendments.	
☐	**Beds 1, 5**	Prepare the ground for green beans (a third of the bed; 2 m²).	
☐	**Bed 2**	Prepare the ground for green beans (whole bed; 6 m²).	
Direct sowing and planting			
☐	**Bed 1**	Sow sweetcorn (a third of the bed; 2 m²; rows 70-80 cm apart, 25-35 cm in the row, 2.5-4 cm deep).	
☐	**Bed 3**	Sow sweetcorn (67% of the bed; 4 m²; rows 70-80 cm apart, 25-35 cm in the row, 2.5-4 cm deep).	
☐	**Bed 4**	Sow sweetcorn (half the bed; 3 m²; rows 70-80 cm apart, 25-35 cm in the row, 2.5-4 cm deep).	

February 2027 field sheet

Ubhejane Crèche garden - tick each job off as it is done.

2 jobs - 2 sowing / planting - 0 harvest / recording

DONE	PLACE	WORK TO COMPLETE	DATE / NOTE
Direct sowing and planting			
☐	**Beds 1, 5**	Sow green beans (a third of the bed; 2 m²; rows 45-60 cm apart, 4-7 cm in the row, 2-5 cm deep).	
☐	**Bed 2**	Sow green beans (whole bed; 6 m²; rows 45-60 cm apart, 4-7 cm in the row, 2-5 cm deep).	

April 2027 field sheet

Ubhejane Crèche garden - tick each job off as it is done.

5 jobs - 0 sowing / planting - 5 harvest / recording

DONE	PLACE	WORK TO COMPLETE	DATE / NOTE
Harvest and record			
☐	**Bed 1**	Harvest green beans (a third of the bed; 2 m²) and sweetcorn (a third of the bed; 2 m²). Record kilograms and where it went.	
☐	**Bed 2**	Harvest green beans (whole bed; 6 m²). Record kilograms and where it went.	
☐	**Bed 3**	Harvest sweetcorn (67% of the bed; 4 m²). Record kilograms and where it went.	
☐	**Bed 4**	Harvest sweetcorn (half the bed; 3 m²). Record kilograms and where it went.	
☐	**Bed 5**	Harvest green beans (a third of the bed; 2 m²). Record kilograms and where it went.	

ImbewuField

FIELD SHEET

August 2027 field sheet

Ubhejane Crèche garden - tick each job off as it is done.

8 jobs - 1 sowing / planting - 0 harvest / recording

DONE	PLACE	WORK TO COMPLETE	DATE / NOTE
Prepare for the next planting			
		Where a bed follows another crop, confirm it is finished and cleared before preparing it. Assess soil and drainage; use a soil test or local advice before adding amendments.	
☐	**Bed 1**	Prepare the ground for turnips (a third of the bed; 2 m²) and spanspek (sweet melon) (a third of the bed; 2 m²).	
☐	**Bed 2**	Prepare the ground for carrots (a third of the bed; 2 m²), beetroot (a third of the bed; 2 m²) and brinjal (eggplant) (a third of the bed; 2 m²).	
☐	**Bed 3**	Prepare the ground for tomatoes (a third of the bed; 2 m²), parsley (a third of the bed; 2 m²) and gem squash (a third of the bed; 2 m²).	
☐	**Bed 4**	Prepare the ground for cucumber (a third of the bed; 2 m²) and green beans (a third of the bed; 2 m²).	
☐	**Bed 5**	Prepare the ground for sweet potato (a third of the bed; 2 m²).	
☐	**Bed 6**	Prepare the ground for lettuce (a third of the bed; 2.667 m²) and groundnuts (peanuts) (a third of the bed; 2.667 m²).	
☐	**Bed 7**	Prepare the ground for peppers (a third of the bed; 2 m²).	
Nursery - raise seedlings			
☐	**Nursery**	Raise and label trays for brinjal (eggplant) (a third of the bed; 2 m²; sow 1.5-2 cm deep) for Bed 2, tomatoes (a third of the bed; 2 m²; sow 1 cm deep) for Bed 3, lettuce (a third of the bed; 2.667 m²; sow 1.5-2 cm deep) for Bed 6 and peppers (a third of the bed; 2 m²; sow 1.5-2 cm deep) for Bed 7. Start checking in Sep; transplant when ready, within the planning window through Nov.	

ImbewuField

FIELD SHEET

September 2027 field sheet

Ubhejane Crèche garden - tick each job off as it is done.

13 jobs - 8 sowing / planting - 0 harvest / recording

DONE	PLACE	WORK TO COMPLETE	DATE / NOTE
Prepare for the next planting			
		Where a bed follows another crop, confirm it is finished and cleared before preparing it. Assess soil and drainage; use a soil test or local advice before adding amendments.	
☐	**Bed 1**	Prepare the ground for peppers (a third of the bed; 2 m²).	
☐	**Bed 4**	Prepare the ground for tomatoes (a third of the bed; 2 m²).	
☐	**Bed 5**	Prepare the ground for cucumber (a third of the bed; 2 m²) and brinjal (eggplant) (a third of the bed; 2 m²).	
☐	**Bed 6**	Prepare the ground for sweet potato (a third of the bed; 2.667 m²).	
☐	**Bed 7**	Prepare the ground for groundnuts (peanuts) (a third of the bed; 2 m²) and gem squash (a third of the bed; 2 m²).	
Nursery - raise seedlings			
☐	**Nursery**	Raise and label trays for peppers (a third of the bed; 2 m²; sow 1.5-2 cm deep) for Bed 1, tomatoes (a third of the bed; 2 m²; sow 1 cm deep) for Bed 4 and brinjal (eggplant) (a third of the bed; 2 m²; sow 1.5-2 cm deep) for Bed 5. Start checking in Oct; transplant when ready, within the planning window through Dec.	
Direct sowing and planting			
☐	**Bed 1**	Sow turnips (a third of the bed; 2 m²; rows 40-60 cm apart, 8 cm in the row, 1.5-2 cm deep) and spanspek (sweet melon) (a third of the bed; 2 m²; rows 150 cm apart, 25-35 cm in the row, 2-3 cm deep).	
☐	**Bed 2**	Sow carrots (a third of the bed; 2 m²; rows 20-40 cm apart, 2-5 cm in the row, 1-2.5 cm deep) and beetroot (a third of the bed; 2 m²; rows 20-30 cm apart, 5-7 cm in the row, 1.5-2 cm deep). From this month, transplant brinjal (eggplant) (a third of the bed; 2 m²; rows 70-80 cm apart, 50 cm in the row) when seedlings and the bed are ready.	

September 2027 field sheet (continued)

DONE	PLACE	WORK TO COMPLETE	DATE / NOTE
Direct sowing and planting (continued)			
☐	**Bed 3**	Sow parsley (a third of the bed; 2 m²; rows 30 cm apart, 10 cm in the row, 1.5-2 cm deep) and gem squash (a third of the bed; 2 m²; rows 100-150 cm apart, 40-50 cm in the row, 2-3 cm deep). From this month, transplant tomatoes (a third of the bed; 2 m²; rows 90-120 cm apart, 30-60 cm in the row) when seedlings and the bed are ready.	
☐	**Bed 4**	Sow cucumber (a third of the bed; 2 m²; rows 120-140 cm apart, 35-50 cm in the row, 2-3 cm deep) and green beans (a third of the bed; 2 m²; rows 45-60 cm apart, 4-7 cm in the row, 2-5 cm deep).	
☐	**Bed 5**	Plant sweet potato slips (a third of the bed; 2 m²; rows 90-100 cm apart, 25-40 cm in the row).	
☐	**Bed 6**	Sow groundnuts (peanuts) (a third of the bed; 2.667 m²; rows 30-45 cm apart, 5-7.5 cm in the row, 5-7.5 cm deep). From this month, transplant lettuce (a third of the bed; 2.667 m²; rows 40-50 cm apart, 25-35 cm in the row) when seedlings and the bed are ready.	
☐	**Bed 7**	From this month, transplant peppers (a third of the bed; 2 m²; rows 60-80 cm apart, 40-50 cm in the row) when seedlings and the bed are ready.	

October 2027 field sheet

Ubhejane Crèche garden - tick each job off as it is done.

5 jobs - 5 sowing / planting - 0 harvest / recording

DONE	PLACE	WORK TO COMPLETE	DATE / NOTE
Direct sowing and planting			
☐	**Bed 1**	From this month, transplant peppers (a third of the bed; 2 m²; rows 60-80 cm apart, 40-50 cm in the row) when seedlings and the bed are ready.	
☐	**Bed 4**	From this month, transplant tomatoes (a third of the bed; 2 m²; rows 90-120 cm apart, 30-60 cm in the row) when seedlings and the bed are ready.	
☐	**Bed 5**	Sow cucumber (a third of the bed; 2 m²; rows 120-140 cm apart, 35-50 cm in the row, 2-3 cm deep). From this month, transplant brinjal (eggplant) (a third of the bed; 2 m²; rows 70-80 cm apart, 50 cm in the row) when seedlings and the bed are ready.	
☐	**Bed 6**	Plant sweet potato slips (a third of the bed; 2.667 m²; rows 90-100 cm apart, 25-40 cm in the row).	
☐	**Bed 7**	Sow groundnuts (peanuts) (a third of the bed; 2 m²; rows 30-45 cm apart, 5-7.5 cm in the row, 5-7.5 cm deep) and gem squash (a third of the bed; 2 m²; rows 100-150 cm apart, 40-50 cm in the row, 2-3 cm deep).	

PLAN VERSUS REALITY

Monthly harvest and field record

Write the month: _____ Team: _____

Write down what actually happened

Record the date, crop, bed and actual harvest weight. Write how much was used, kept, shared or lost. These records help you check the next plan.

Harvest record

Date	Crop / bed	Picked kg	Used kg	Stored kg	Sold/shared kg	Lost kg

PLAN VERSUS REALITY

Fruit, eggs, honey and other production

Write the month: _____ Team: _____

Use the unit you actually measured

Write the food and its source: tree, coop, hive or bed. Use kg for weighed food, eggs for counted eggs, or jars, bunches or items. Record jar size in the source column. Keep all amounts on one row in the same unit.

Date	Food / source	Collected	Unit	Used	Sold/shared	Lost

Weekly observation

Week	Rainfall	Irrigation	Pests / disease	What we observed	What we changed

Decision for next month

Observe. Adjust. Write it down.
